

Work description report

Here is what was done during the last weeks, July 06 to July 16.

I. Exterior works:



After you left we had serious discussions with several contractors about the outdoor toilets. This took us some time to find the best ones. Some were too expensive some too busy and finally after a week we managed to agree with one team of contractors. The works started on 12th of July which is a bit late but it just could not happen earlier.



We hired more people than usual in order to speed up the works which are going good so far. The brother from the church who did the drawing of the toilets came to help.



the walls of the toilets are rising fast.




the water installation around the toilets is being installed and the main property sewage is dug up as you see on the above right photo.



The plumber team working hard connecting the toilets to the main property sewage.



More windows installed
a lot of trees are gone and still more to go. The water well is concreted and ready for the water pump to be installed. Waiting for the water company to install it.

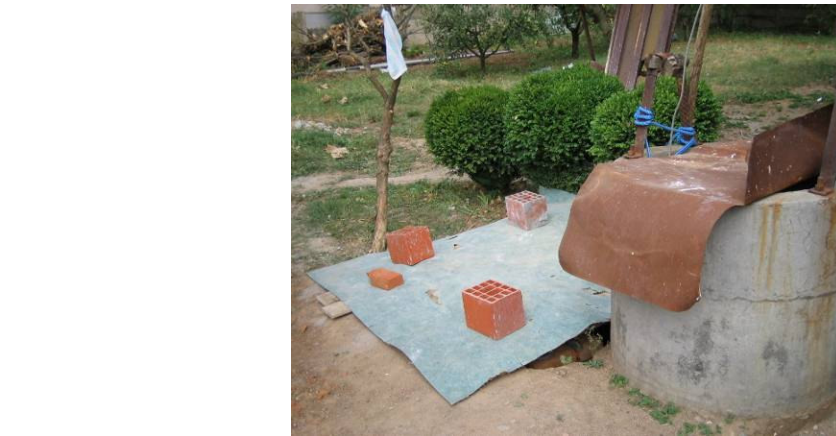


The water well is concreted and ready for the water pump to be installed. Waiting for the water company to install it.

II. INTERIOR WORKS




The chimney is built in case we need to heat up on fire wood. The upstairs rooms are ready for painting as well as the stair walls. The old doors upstairs are being refreshed as the new ones are expensive.

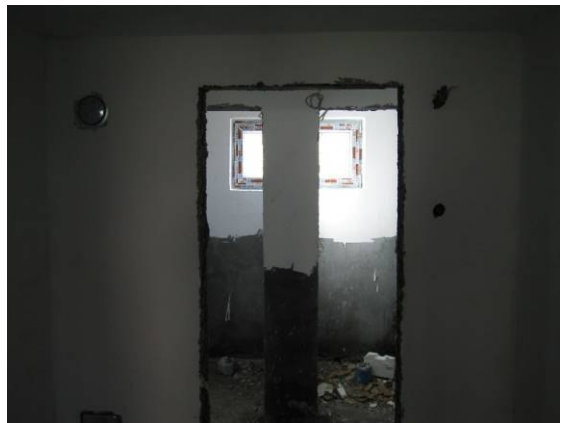



The first floor walls are also ready for painting. The downstairs toilets are being prepared. The tiles will be put soon in both toilets upstairs and downstairs.

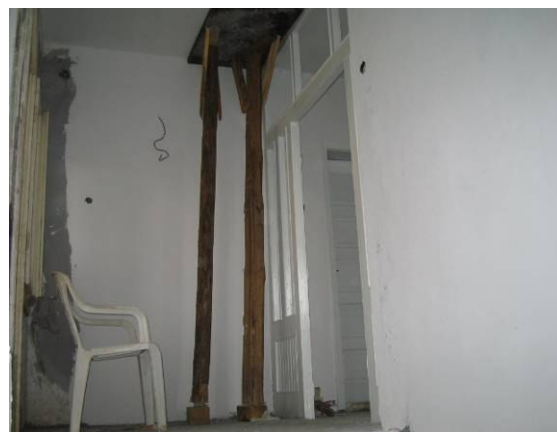

The electricity work is being done bit by bit. Both down and upstairs and also on the attic.

On behalf of CC board

Emanuel
